M55 HEYHOUSES MILESTONE CHART

ID	Ta: Mo	Task Name	Duration	Start	Finish	% Comp.
		Milestone: Yes	**2508d**			**28%**
1		Planning permission secretary of State	240 days	Thu 01/09/11	Wed 01/08/12	100%
3		**Fylde Borough agree fin**	1 day	Mon 03/08/15	Mon 03/08/15	100%
8		**Approval HCA-Kensingto**	113 days?	Mon 03/04/17	Wed 06/09/17	75%
10		WA Detail design and contract documentation completed	188 days	Tue 07/02/17	Thu 26/10/17	72%
11		Risk Assessment Worksho	1 day	Wed 06/09/17	Wed 06/09/17	70%
14		Post Design agreement	49 days	Fri 27/10/17	Wed 03/01/18	0%
15		**Submit Cabinet report Lancashire CC finance**	20 days	Fri 02/06/17	Wed 26/07/17	100%
16		Produce SOBC case for HE and LEP	7.8 days	Mon 03/04/17	Mon 30/10/17	76%
18		WSP HE Independent Ass	10 days	Mon 30/10/17	Mon 13/11/17	0%
19		HE Value Management Workshop	1.15 days	Mon 06/11/17	Tue 07/11/17	0%
20		HIF funding submission	20 days	Fri 01/09/17	Thu 28/09/17	0%
21		**Funding Approval HE**	21 days	Fri 18/08/17	Tue 28/11/17	25%
22		submission NPIF	16 days	Fri 09/06/17	Fri 30/06/17	100%
23		**HIF funding Approval**	44 days	Fri 01/12/17	Wed 31/01/18	0%
24		**NPIF approval**	32 days	Thu 16/11/17	Fri 29/12/17	0%
25		**Scheme Funding Approval LCC**	49 days	Mon 08/01/18	Thu 15/03/18	0%
26		Atkins Independent Assurance	13 days	Mon 19/03/18	Wed 04/04/18	0%
27		**Funding TFL approval**	1 day	Wed 04/04/18	Wed 04/04/18	0%
28		**Approval from LEP**	1 day	Tue 24/04/18	Tue 24/04/18	0%
29		Growth Deal approval	14 days	Wed 25/04/18	Mon 14/05/18	0%
37		Prepare PQQ	11 days	Fri 15/09/17	Fri 29/09/17	100%
38		specification BoQ contract docs	20 days	Fri 29/09/17	Thu 26/10/17	5%
39		Review and OJEU	40 days	Fri 27/10/17	Thu 21/12/17	0%
40		Tender & pre award meeti	60 days	Fri 22/12/17	Thu 15/03/18	0%
41		Stakeholder signoff & award contract	40 days	Thu 05/04/18	Wed 30/05/18	0%
42		Mobilise	40 days	Thu 31/05/18	Wed 25/07/18	0%
43		Contractor set up and preliminary works	58 days	Thu 26/07/18	Mon 15/10/18	0%
44		Construction	650 days	Tue 16/10/18	Mon 12/04/21	0%
51		Wild Lane sustainable roul	90 days	Wed 04/11/20	Tue 09/03/21	0%

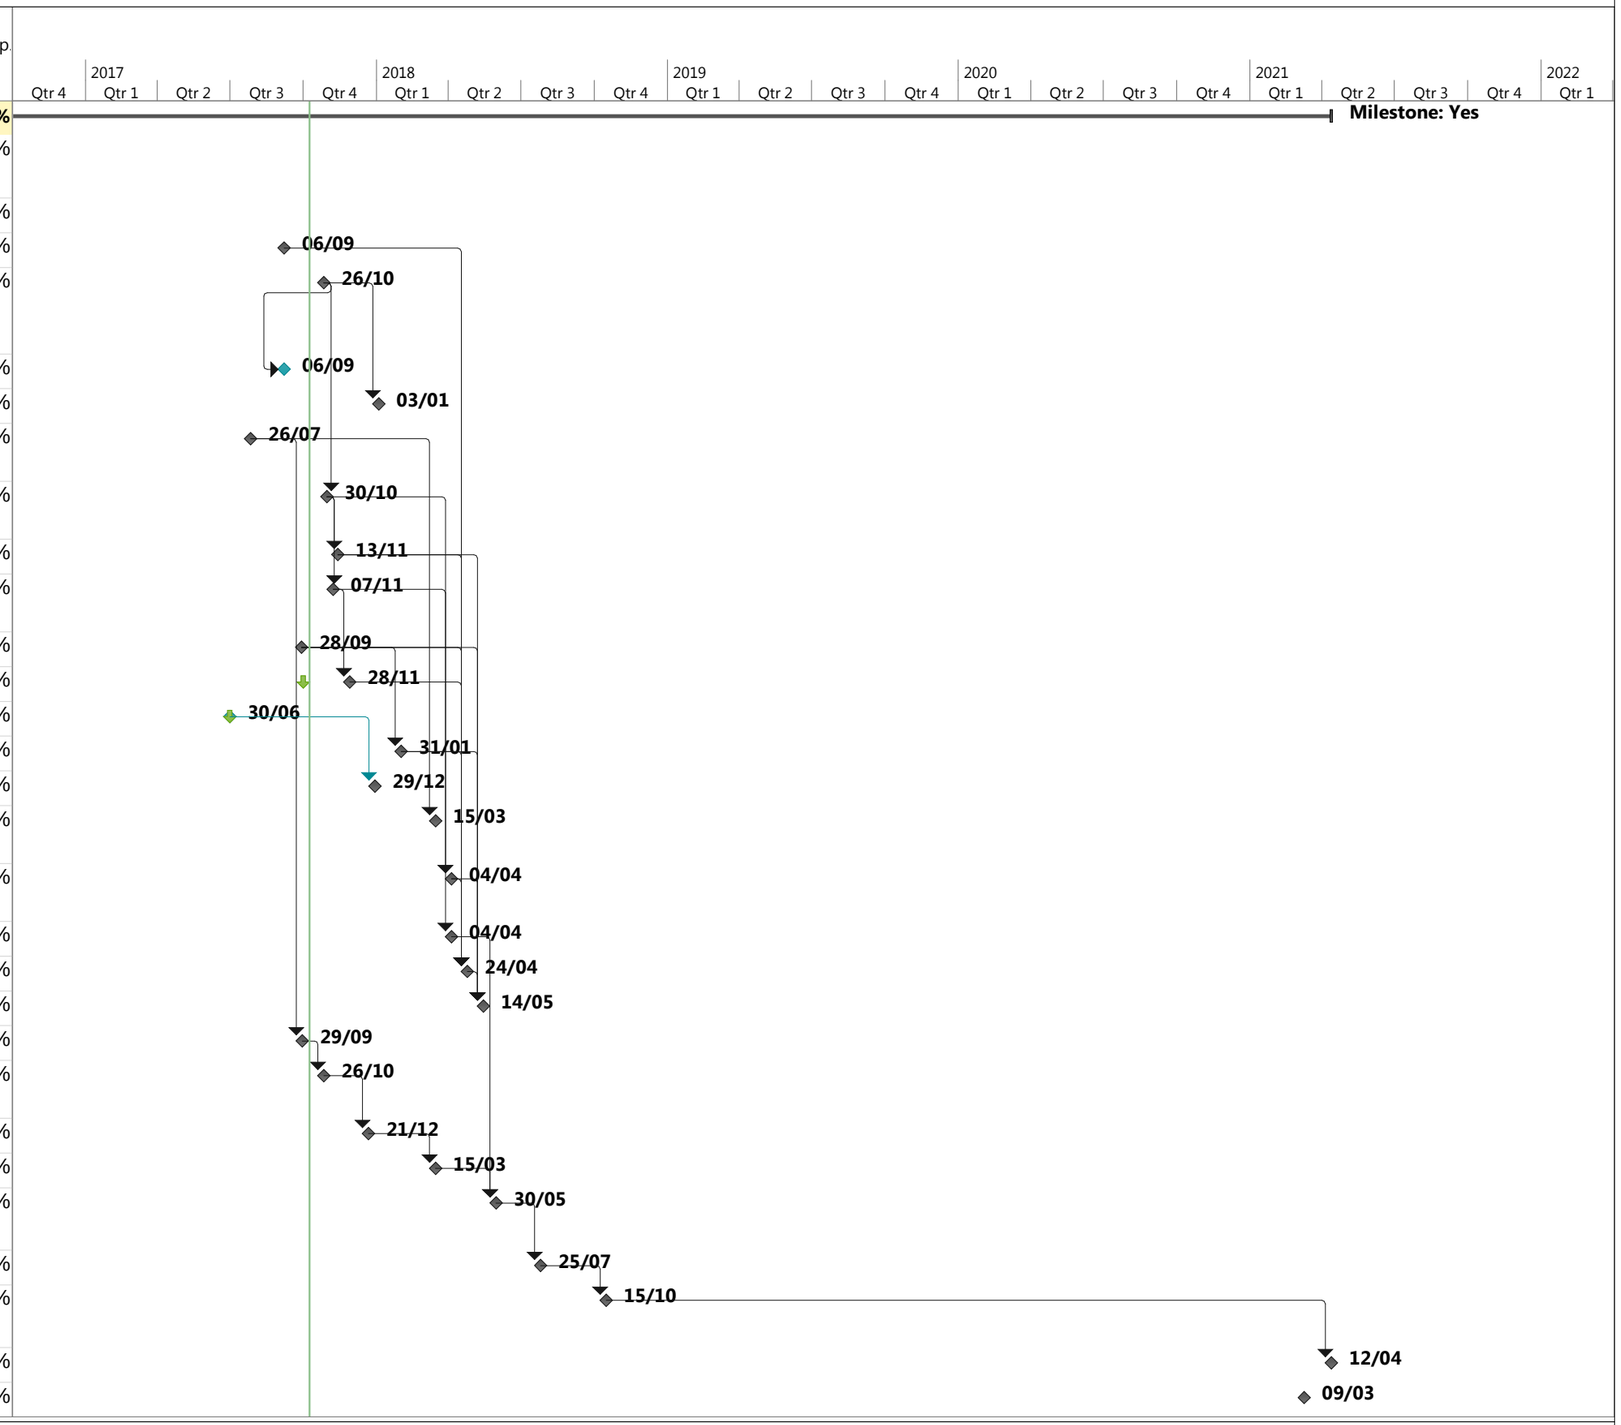

Project:
Pre Project M55 tender to cons
Date: Mon 09/10/17

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
